


ROAD CLOSURES!


- JACK JONES ROAD, from Boyd Cowart Road to N. Hollandtown Road – Closed due to collapsed bridge.
- ALTON CARLTON ROAD, from W. Main Street to the bridge – Closed due to road damaged.

For update information, contact: Road and Bridge Department, tel. 863-773-3272.

FDOT FUTURE PROJECTS

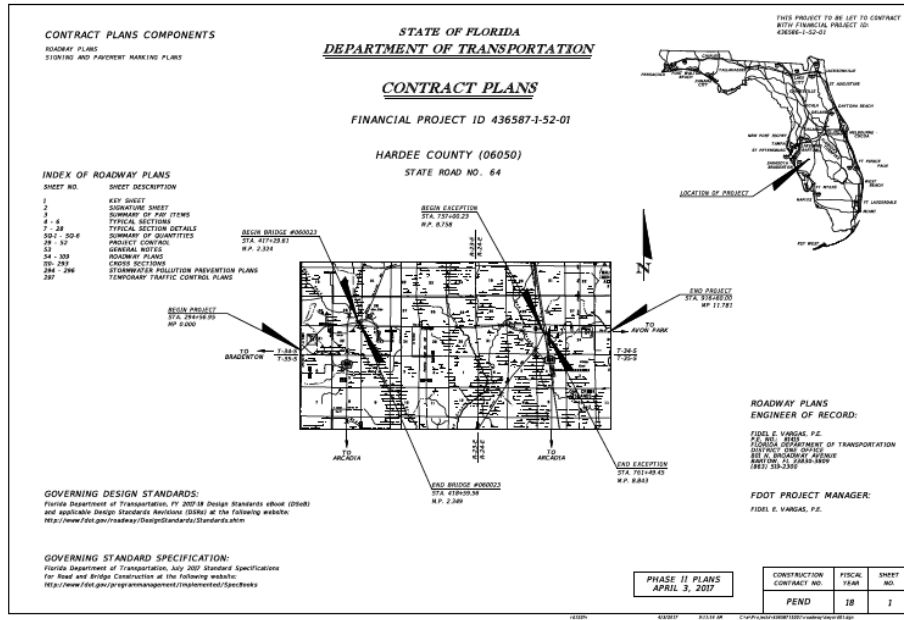

SR 64 MILLING AND RESURFACING: The Florida Department of Transportation (FDOT) will be implementing Project ID 436587-1-52-01, milling and resurfacing of SR 64 from Taylor Road to West Main Street, in Hardee County. The FDOT has prepared the preliminary construction plans for review and comments. If you have any questions, please contact the FDOT, District 1, Bartow, tel. 863-519-2300.

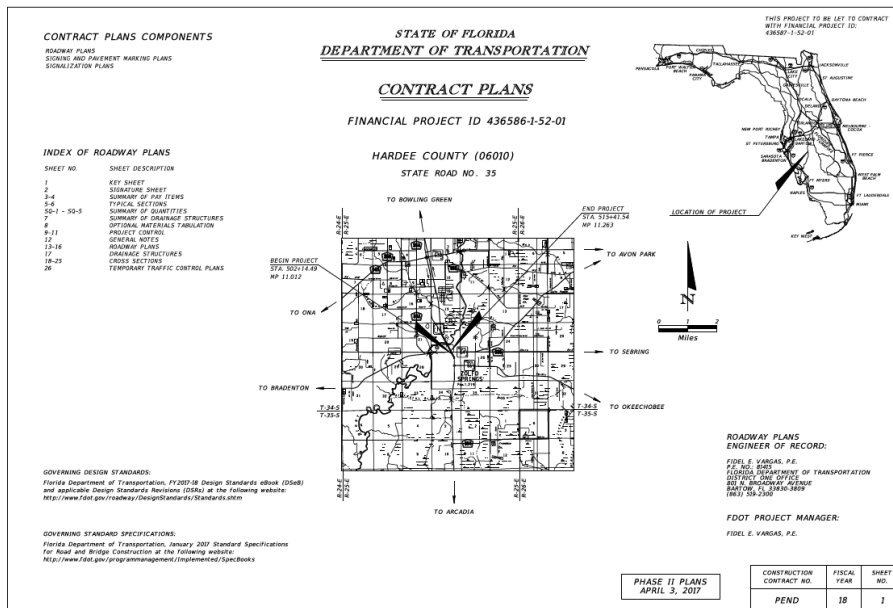

SR 35 (US 17) and SR 64 INTERSECTION MILLING AND RESURFACING:

The Florida Department of Transportation (FDOT) will be implementing Project ID 436586-1-52-01, milling and resurfacing of the SR 35 and SR 64 intersection, in Hardee County. The FDOT has prepared the preliminary construction plans for review and comments. If you have any questions, please contact the FDOT, District 1, Bartow, tel. 863-519-2300.

HARDEE COUNTY ROAD AND BRIDGE DEPARTMENT

1. JOHNSTON ROAD - BRIDGE #64112 REPLACEMENT: COMPLETE.

The project consists of replacing one lane timber bridge, approximately 180 linear feet, with multiple aluminum box culverts. A roadway, with two lanes, will be constructed over the culverts. The roadway will be surfaced with chip seal consisting of four layers of stone and asphalt emulsion.

2. ED WELLS ROAD: COMPLETE

The project consists of chip seal work on Ed Wells Road, from West Main Street (SR 636) up to Rhynn Road.

3. SASSER ROAD, WEST SIDE: COMPLETE

The project consists of chip seal work on Sasser Road, West side, from Merle Langford Road to Moffitt Road. One lane of the road will be closed during construction.

4. SUMNER ROAD, FROM BOYD COWART ROAD TO NORTH CURVE: COMPLETE.

The project consists of chip seal work within the limits from Boyd Cowart Road to the north curve. Leveling work will be performed as needed prior to the chip sealing of the roadway. The leveling work uses hot mix asphalt to fill in potholes and level areas in preparation of the chip sealing. The leveling work, which often looks like patch work, will be allowed to cure at least at a week, then chip seal is placed over the whole roadway. The chip sealing consists of the placement of up to three layers of asphalt emulsion and stones and compacted with a road roller. Loose stones are commonly expected after the chip seal work, which will be swept after a couple weeks. The time prior to sweeping allows additional time for the stones to adhere with the emulsion. Then the completed chip sealed roadway will be opened to traffic.

5. SKIPPER ROAD, FROM PARNELL ROAD TO SOUTH HAMMOCK ROAD: COMPLETE.

The Road and Bridge Department will perform re-grading and chip seal work on Skipper Road, from Parnell Road to South Hammock Road.

6. FARRELL ROAD, FROM SR 66 TO SR 64: COMPLETE.

The project consists road surface re-grading and chip seal work, from SR 66 to SR 64.

7. JOHN GILL ROAD - BRIDGE #64098 REPLACEMENT: COMPLETE.

The project consists of replacing the one lane timber bridge with multiple pipes. The one lane timber bridge, approximately 53 linear feet, will be replaced with multiple aluminum pipes. A two lanes roadway will be constructed over the pipes. The roadway surfacing over the pipes will be performed in conjunction with the second phase of the John Gill Road surfacing project.

8. JOHN GILL ROAD, FROM SR 62 TO BRIDGE. – Road Open To Local Traffic.

The project consists of road re-grading and surfacing work, from SR 62 to the new bridge #64098.

- Start Date: Road work will commence upon completion of the John Gill Road Bridge Replacement project.
- Estimated Completion Date: Rain delay.
- The road is presently open to local traffic only. The road will be closed when the work starts for re-grading and chip sealing. During that time motorists are advised to use other routes during the construction period.

9. DOC COIL ROAD, FROM CR 664 TO DIXIANA DRIVE: COMPLETE.

The project consists of road surface re-grading and chip seal work, from SR 664 to Dixiana Drive. The work includes Parish Road between CR 664 and Doc Coil Road.

10. McDONALD ROAD, FROM METHENY ROAD TO OLD BRADENTON ROAD: COMPLETE.

The project consists of road surface re-grading and chip seal work, from Old Bradenton Road to Metheny Road.

11. TERRELL ROAD, FROM LOUISIANA STREET TO METHENY ROAD: PAVING COMPLETE.

The project consists of road surface widening and resurfacing with hot mix asphalt, from Louisiana Street to Metheny Road. The motoring public is advised to slow down and follow the temporary traffic signs and flagging within the construction zone.

- Start date: August 7, 2017.
- Estimated Completion Date: August 14, 2017.
- Pavement markings and striping – to be scheduled. (Rain delay)

12. PAULA DRIVE, FROM GULFVIEW DRIVE TO CUL-DE-SAC: COMPLETE.

The project consists of road resurfacing with hot mix asphalt.

13. WILL DUKE ROAD, FROM US 17 SB TO US 17 NB: COMPLETE.

The project consists of road resurfacing with hot mix asphalt.

14. OTHER:

- **Doc Coil Road, from US 17 to Dixiana Drive, Bowling Green:**

The road resurfacing project was delayed due to a drainage improvement and sidewalk construction by the FDOT and City of Bowling Green.

- **WILL DUKE ROAD, FROM MARTIN L. KING, JR. AVENUE. TO US 17 NB:**

The road resurfacing project was delayed due to a water main construction by the IDA.

15. FUTURE ROADS AND BRIDGE IMPROVEMENT PROJECTS:

The Road and Bridge Department will be performing other road and bridge improvements in the future. The following projects will be evaluated for construction funding. This list is subject to change.

- Parnell Bridge #64034.
- Murphy Road Bridge #64105.
- John Gill Road surfacing, from bridge to Ollie Roberts Road.
- Ander Marsh Road, surfacing, from West Main Street to Dansby Road.
- Theatre Road, from SR 62 to Bostick Road.
- Greenleaf Road, from Steve Robert Special to Lockmilller Road (W-E).
- Lockmilller Road (N-S), from SR 64 to Lockmilller Road (W-E).
- Lockmilller Road (W-E), from SR 64 to Lockmilller Road (N-S).
- Garza Road, from Steve Robert Special to SR 66.
- Ralph Johns Road, from SR 64 to Dansby Road.
- George marsh Road, from Crewsville Road to Sweetwater Road.

For more information, contact: Road and Bridge Department, tel. 863-773-3272.

WORK BY OTHERS

- **HEARD BRIDGE ROAD – TEMPORARY ROAD CLOSURE AND BY-PASS**

- Mosaic Fertilizer LLC plans to construct three 36 inches diameter steel casings and perform a dragline equipment crossing on Heard Bridge Road. A temporary road will be constructed allowing the motoring public to by-pass the work area. The temporary by-pass road will have a 15 MPH speed limit. The motoring public is advised to slow down and follow the temporary traffic control signs and flagging within the construction zone.

Start Date: To be determined.

Construction duration: 5 days, approx.

Contact: Kimley-Horn, Inc., attn.: Bo Conerly, P.E., tel. 863-226-6857.

- **MARTIN LUTHER KING AVE. AND WILL DUKE ROAD, FROM US 17 NORTH BOUND TO BAY STREET**

The Industrial Development Authority (IDA) plans to construction water mains along Will Duke Road and Martin Luther King, Jr. Avenue, from U.S. 17 North Bound to Oak Street. The roads will be open to traffic during construction. The motoring public is advised to slow down and follow the temporary traffic signs and flagging within the construction zone.

Start Date: To be determined.

Construction duration: To be determined.

Contact: Chastain-Skillman, Inc., attn.: Doug Jones, P.E., tel. 863-646-1402.

- **XX**
